



Melville Moreland Shopping Strip

Construction Project Update No. 3 4 April 2022

Council is improving areas along the Melville Moreland Shopping Strip, Brunswick West. The project aims to revitalise the shopping strip and improve pedestrian amenity, walkability, safety and street presentation.

What is happening?

During the past weeks:

- Stage 1 of the project is completed, with Stage 2 is wrapping up soon.
- Some small areas may still not be fully accessible. Please ensure that you are walking safely around the temporary bollards.
- All the landscaping works, including low-level plants and trees will be done at the end of the project.

What is coming?

Over the next fortnight:

- We have revised the staging plan, as shown overleaf.
- In the next fortnight we are working on Stage 3, which now combines three areas to expedite the project. The works will include demolition, excavation, kerb and channel and footpath works.

Learn More

Online

www.conversations.moreland.vic.gov.au/melville-moreland-streetscape-improvements

In Person

Call Tri Setyani on 9240 2471 or email tsetyani@moreland.vic.gov.au

More information

Minor updates to our construction plan will be updated on the website listed above. Any significant changes will be hand delivered to affected properties as early as possible.

Moreland Language Link

廣東話 9280 1910
Italiano 9280 1911
Ελληνικά 9280 1912

عربي 9280 1913
Türkçe 9280 1914
Tiếng Việt 9280 1915

हिंदी 9280 1918
普通话 9280 0750
ਪੰਜਾਬੀ 9280 0751

All other languages
9280 1919

Melville Moreland Shopping Strip


Construction Project Update No. 3 4 April 2022

Staging Plan

4 April 2022 update

Working hours: 5 am-5 pm. The site foreman will notify affected properties before the works to adjust the working hours.

Nightworks: 7 pm-5 am, if required for areas outside residential areas.

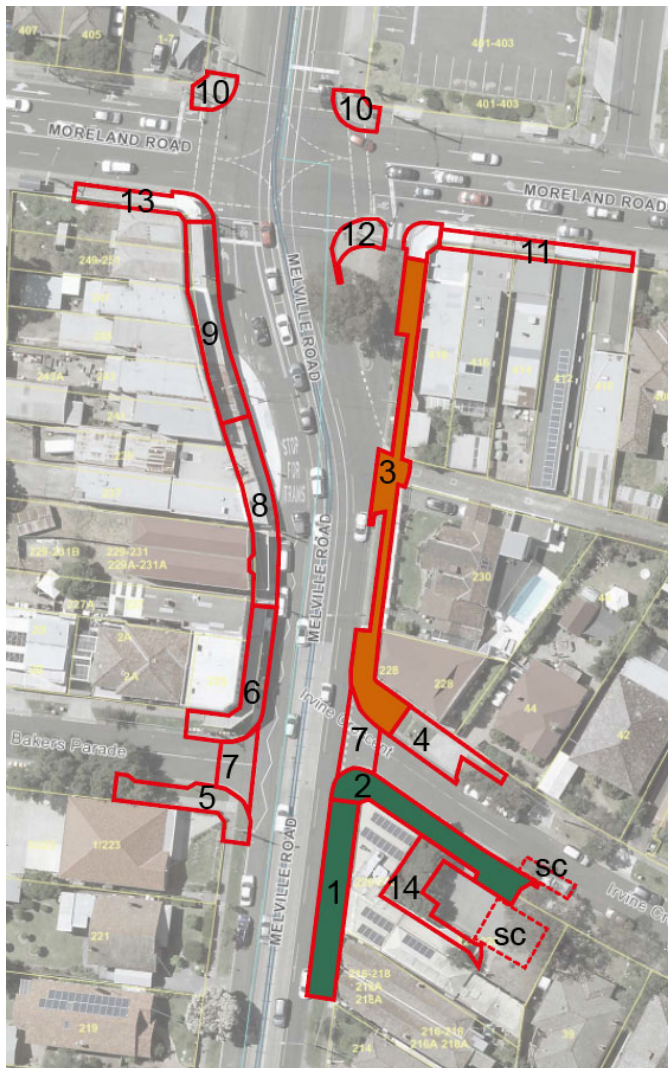

STAGE	DATE	Approximate Duration and Status
	Site establishment & survey 10 -16 March 2022	Completed
1	16 March – 1 April 2022	Completed
2	21 March – 5 April 2022	Completed
3	4 April – 20 April 2022	2 weeks
4	To be advised	1 week
5	To be advised	1.5 weeks
6	To be advised	1.5 weeks
7	To be advised	1.5 weeks
8	To be advised	1.5 weeks
9	To be advised	1.5 weeks
10	To be advised	1.5 weeks
11	To be advised	1.5 weeks
12	To be advised	1.5 weeks
13	To be advised	1.5 weeks
14	To be advised	1.5 weeks
SC	Site Compound storage 10 March until the end of construction project	

Moreland Language Link

廣東話 9280 1910
Italiano 9280 1911
Ελληνικά 9280 1912

عربي 9280 1913
Türkçe 9280 1914
Tiếng Việt 9280 1915

हिंदी 9280 1918
普通话 9280 0750
ਪੰਜਾਬੀ 9280 0751

All other languages
9280 1919
