



Melville Moreland Shopping Strip

Construction Project Update No. 4 2 May 2022

Council is improving areas along the Melville Moreland Shopping Strip, Brunswick West. The project aims to revitalise the shopping strip and improve pedestrian amenity, walkability, safety and street presentation.

What is happening?

During the past weeks:

- Stage 3 and 4A of the project are completed (please see diagram).
- Due to the raingarden construction's delay, Irvine Cr connection to Melville Rd will remain closed. While we are resolving the issue, please use other exits. Please let the Site Foreman know if you need to access the road urgently. We apologise for the inconvenience.

What is coming?

Over the next fortnight:

- Stage 4B, 4C and 5 will commence.
- The lane on the East side of Melville Rd will be closed to traffic for a week. Please use the lane's exit to Irvine Cr.
- The works for the coming stages will include demolition, , kerb and channel and footpath works.

Learn More

Online

www.conversations.moreland.vic.gov.au/melville-moreland-streetscape-improvements

In Person

If you have any questions regarding the construction works please contact:

- Site Foreman, Darian Lindsay from Blue Peak Constructions on 0433 982 963
- For other enquiries please contact: Council's Principal Urban Designer, Tri Setyani on 9240 2471 or via email tsetyani@moreland.vic.gov.au

Moreland Language Link

廣東話 9280 1910
Italiano 9280 1911
Ελληνικά 9280 1912

عربي 9280 1913
Türkçe 9280 1914
Tiếng Việt 9280 1915

हिंदी 9280 1918
普通话 9280 0750
ਪੰਜਾਬੀ 9280 0751

All other languages
9280 1919


Melville Moreland Shopping Strip

Construction Project Update No. 4 2 May 2022

Staging Plan

Working hours: 5 am-5 pm. The site foreman will notify directly adjacent properties before the works to adjust the working hours. **Early morning works** between 5am – 9am will be required for sites on the east side of Moreland Rd (such as stage 2, 3 and 4 due to the clearway, VicRoads and yarra Tram 's requirement.

Nightworks: 7 pm-5 am, if required for areas outside residential areas.

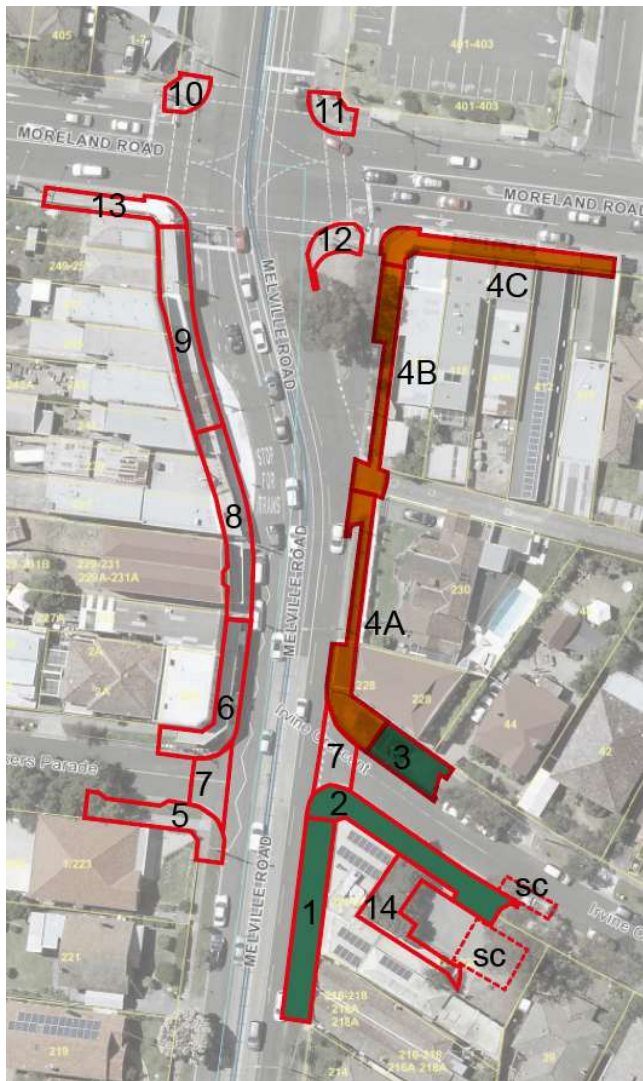

STAGE	DATE	Approximate Duration and Status
	Site establishment & survey 10 -16 March 2022	Completed
1	16 March – 1 April 2022	Completed
2	21 March – 5 April 2022	Completed
3	4 April – 2 May 2022 <i>Irvine Cr road closure (to Melville Rd) until further advice, please use other exits</i>	Completed (by Monday 2 May 2022)
4A	25 March– 2 May 2022	Completed
4B	2 May 2022 (demolition starts) <i>Lane closure (to Melville Rd) from 16 May 2022, please use other exits</i>	1 week
4C	2 nd of May (demolition starts)	1.5 week
5	16 of May 2022	1.5 weeks
6	To be advised	1.5 weeks
7	To be advised	1.5 weeks
8	To be advised	1.5 weeks
9	To be advised	1.5 weeks
10	To be advised	1.5 weeks
11-14	To be advised	1.5 weeks
SC	Site Compound storage - 10 March until the end of construction project	1.5 weeks

Moreland Language Link

廣東話 9280 1910
Italiano 9280 1911
Ελληνικά 9280 1912

عربي 9280 1913
Türkçe 9280 1914
Tiếng Việt 9280 1915

हिंदी 9280 1918
普通话 9280 0750
ਪੰਜਾਬੀ 9280 0751

All other languages
9280 1919
