



Melville Moreland Shopping Strip

Construction Project Update No. 6 7 June 2022

Council is improving areas along the Melville Moreland Shopping Strip, Brunswick West. The project aims to revitalise the shopping strip and improve pedestrian amenity, walkability, safety and street presentation.

What is happening?

During the past weeks:

- Demolition works for Stage 5, 6, 7 and 8 had commenced.
- Shopfront activation works (shop display upgrade) are underway for shops within the completed stages.
- Following Council decision, Footpath Trading Permits will be discounted by 50% for the 22/23 financial year.

What is coming?

Over the next weeks:

- Concrete pouring for Stage 5, 6, 7 and 8 will be communicated with businesses to avoid disruption.
- Street parking will be affected in front of shops for the kerb works. We are working through this part of the work as fast as we can. We apologise for the inconvenience.

Learn More

Online

www.conversations.moreland.vic.gov.au/melville-moreland-streetscape-improvements

In Person

If you have any questions regarding the construction works please contact:

- Site Foreman, Darian Lindsay from Blue Peak Constructions on 0433 982 963
- For other enquiries please contact: Council's Principal Urban Designer, Tri Setyani on 9240 2471 or via email tsetyani@moreland.vic.gov.au

Moreland Language Link

廣東話 9280 1910
Italiano 9280 1911
Ελληνικά 9280 1912

عربي 9280 1913
Türkçe 9280 1914
Tiếng Việt 9280 1915

हिंदी 9280 1918
普通话 9280 0750
ਪੰਜਾਬੀ 9280 0751

All other languages
9280 1919

Melville Moreland Shopping Strip


Construction Project Update No. 6 7 June 2022

Staging Plan

Working hours: 5am-5pm. The site foreman will notify directly the adjacent properties before the works to adjust their working hours.

Early morning demolition works between 5am – 9am may be required for the first day of the demolition of each stage for the purpose of adjusting to the businesses' opening hours. After Stage 8 (7 June), there will be no additional early morning demolition works.

The staging dates are subject to weather conditions. Wet weather may delay the planned completion dates due to concrete curing's requirement.

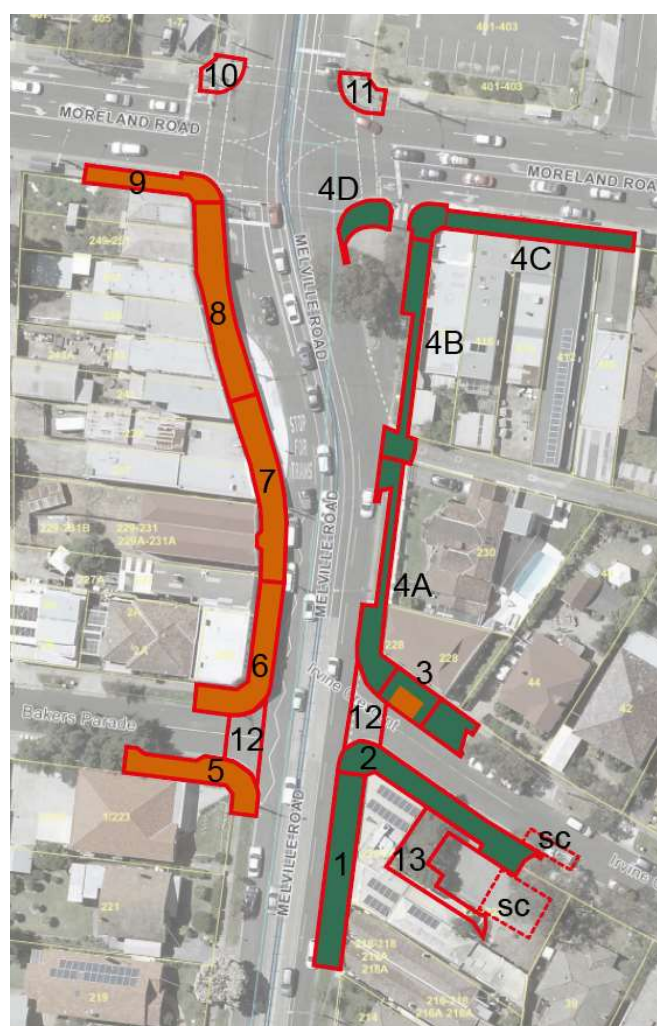

STAGE	DATE	Status / Duration
	Site establishment & survey 10 -16 March 2022	Completed
1	16 March – 1 April 2022	Completed
2	21 March – 5 April 2022	Completed
3	4 April – 2 May 2022 Irvine Cr road closure (to Melville Rd) until further advice, please use other exits	Completed, except for the raingarden landscaping
4	25 March – 27 May 2022	Completed
5	15 June – 17 June 2022	Ongoing: 1 week
6	30 May – 17 June 2022 Bakers Pd road closure will be required for stage 5 & 6, please use other exits	2 weeks
7	30 May – 22 June 2022	2 weeks
8	7 June – 22 June 2022	2 weeks
9	21 June – 27 June 2022	1 week
10-11	To be advised	Upcoming: 2 weeks
12	To be advised	2 weeks
13	To be advised	2 weeks
SC	Site Compound storage - 10 March until the end of construction project	

Moreland Language Link

廣東話 9280 1910
Italiano 9280 1911
Ελληνικά 9280 1912

عربي 9280 1913
Türkçe 9280 1914
Tiếng Việt 9280 1915

हिंदी 9280 1918
普通话 9280 0750
ਪੰਜਾਬੀ 9280 0751

All other languages
9280 1919
