

# Melville Moreland Shopping Strip


Construction Project Update No. 6 7 June 2022

## Staging Plan

**Working hours:** 5am-5pm. The site foreman will notify directly the adjacent properties before the works to adjust their working hours.

**Early morning demolition works** between 5am – 9am may be required for the first day of the demolition of each stage for the purpose of adjusting to the businesses' opening hours. After Stage 8 (7 June), there will be no additional early morning demolition works.

The staging dates are subject to weather conditions. Wet weather may delay the planned completion dates due to concrete curing's requirement.

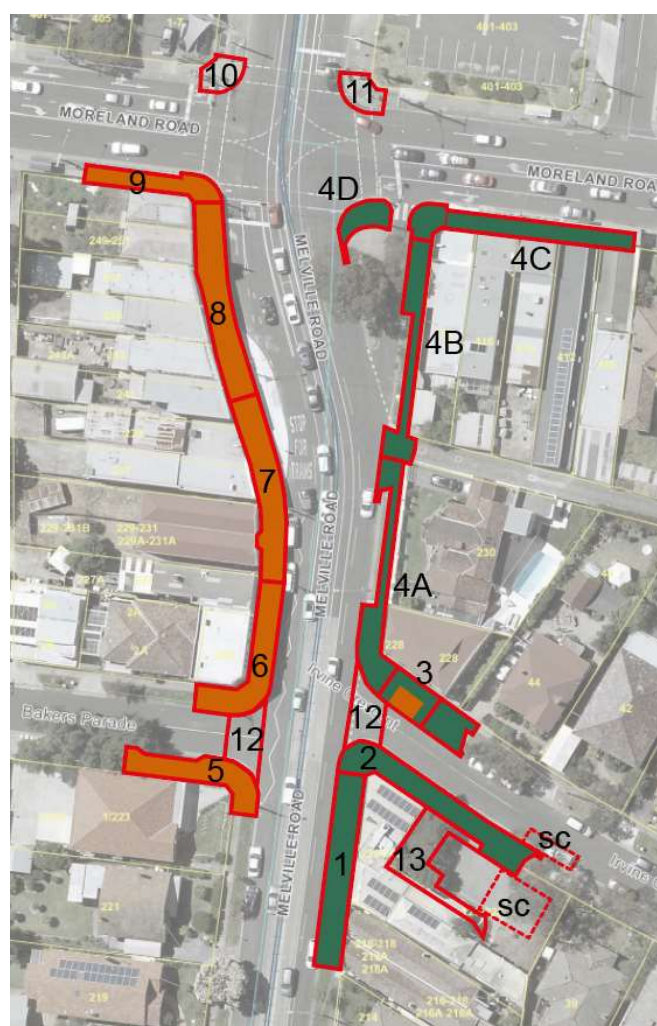

STAGE	DATE	Status / Duration
	Site establishment & survey 10 -16 March 2022	Completed
1	16 March – 1 April 2022	Completed
2	21 March – 5 April 2022	Completed
3	4 April – 2 May 2022 <b>Irvine Cr road closure (to Melville Rd) until further advice, please use other exits</b>	Completed, except for the raingarden landscaping
4	25 March – 27 May 2022	Completed
5	15 June – 17 June 2022	Ongoing: 1 week
6	30 May – 17 June 2022 <b>Bakers Pd road closure will be required for stage 5 &amp; 6, please use other exits</b>	2 weeks
7	30 May – 22 June 2022	2 weeks
8	7 June – 22 June 2022	2 weeks
9	21 June – 27 June 2022	1 week
10-11	To be advised	Upcoming: 2 weeks
12	To be advised	2 weeks
13	To be advised	2 weeks
SC	Site Compound storage - 10 March until the end of construction project	

### Moreland Language Link

廣東話 9280 1910  
Italiano 9280 1911  
Ελληνικά 9280 1912

عربي 9280 1913  
Türkçe 9280 1914  
Tiếng Việt 9280 1915

हिंदी 9280 1918  
普通话 9280 0750  
ਪੰਜਾਬੀ 9280 0751

All other languages  
9280 1919
